


JAIL PROJECT JULY STATUS REPORT TO BOARD OF SUPERVISORS

I. Achievements the past month (July)

A. Construction:

1. Site Work (Contractor: Ferguson Hall)
 - a. All building pads were completed on July 3. SB2 and Housing Unit HB were 6 days behind schedule, due to weather; the remaining building pads were completed on the original schedule.
 - b. All storm sewer pipes have been installed, without manholes and inlets.
 - c. Approximately 450 more feet of subsurface drainage tile was installed below the future parking lot to drain springs (change order 1.01-2 processed by Board of Supervisors in May).
2. Precast masonry Cells (Oldcastle): Cell molds have been delivered to the Manchester Plant.
3. General Contractor (Horning Construction)
 - a. Exterior foundation walls and footings complete for buildings SB2, the sally port in SB1, and housing units HB, HC, & HD. Interior footings for cells have been completed for HB & most of SB2. Exterior footing started on Housing units HE & HF.
4. Structural Steel & Miscellaneous Metal Contractor (Rochester Rigging):
 - a. Delivered structural plates, anchor bolts, bearing plates that are embedded in concrete by the GC.
 - b. Received approval on steel joist & decking drawings.
5. Plumbing & Fire Suppression Contractor (Ferraiulo Plumbing & Heating):
 - a. Began installation of piping under housing unit HB and SB2 (kitchen area).
 - b. Delivered to site water line and sanitary sewer piping for precast cell chases, and gas line pipe for the exterior of the building.
6. HVAC Contractor (John W. Danforth): Fabricated and delivered all ductwork for all Housing Units (wanted to complete prior to start of large school contracts in fall).
7. Electrical Contractor (Blackmon Farrell)
 - a. Finished communication (telephone & cable) duct banks from County Road 46 to the area immediately outside SB6 (awaiting foundation completion to finish)
 - b. Began work on underground conduit in HB & SB2.
8. Detention Equipment and Electronic Security:
 - a. Began work on security system panel layout & screen layout.
 - b. Finished keying plan for entire building.
 - c. Began fabrication of hollow metal doorframes & embeds (steel plate that connects to masonry to which the door frames are later welded).

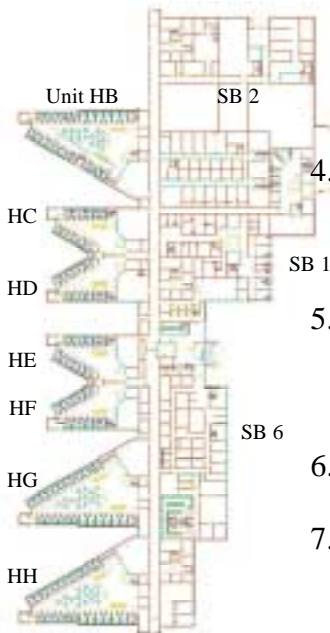

B. Construction Manager (Pike Construction: Coordinated delivery of embeds with Security and Detention Equipment Contractor to ensure that General Contractor's masonry work will not be delayed.

C. Architect:

1. Completed waterline redesign drawings for ductile iron 16-inch pipe, and submitted to the Hopewell Water District and New York State Dept. of Health for Review.
2. Processed 47 of 54 contractor requests for information to date. None are overdue.

II. Issues


A. Waterline agreement with Hopewell/Canandaigua Water District.

Respectfully Submitted by Thomas P. Harvey AICP

**JAIL PROJECT
JULY STATUS REPORT TO BOARD OF SUPERVISORS**

III. Planned for August

Progress



A. Construction Manager:

1. Progress meetings held weekly on Tuesday mornings.
2. Continue vigilance concerning Hollow Metal Door delivery and coordination

B. Construction/Contractors

1. Site work: Ferguson Hall will install manholes and drop inlets (precast structures) to be installed. Water line installation will continue.
2. Precast: On August 16 will provide evaluation cell, including all internal and external finishes and furniture for evaluation.
3. General Construction: Continue exterior foundation walls & footers on remaining housing units HG and HH, and the remainder of SB1, and start SB6. Masons will begin construction on the exterior concrete block walls on SB2 and Housing Unit HB.
4. Structural Steel: Will deliver lintels, nosing angles for use in masonry walls. Subcontractors will begin fabrication of joists and metal decking.
5. Plumbing Work: will continue underground piping in SB2 and other housing units.
6. HVAC: Will complete fabrication of ductwork for SB1, SB2, & SB6.
7. Electrical work: Continue conduit installation in SB2 & HB, and begin in other Housing Units. Will also work with masons to install conduit in concrete block walls in Housing Unit HB & SB2 as the walls are erected.
8. Detention Equipment: Will begin delivery of doorframes & embeds. Work with masons to install conduit for security equipment (door controls, monitors, intercom system) in concrete block walls in Housing Unit HB & SB2 as the walls are erected.

C. Jail Project Committee:

1. Bidding of mobile food carts (item that was taken out of Kitchen Contractors Bid).
2. Schedule will be reviewed on August 21, 2002.

D. Architect: Review precast cell mock-up, masonry mockup of exterior block & brick walls.

IV. Photos



Footers at SB2



SB2 Footers at Medical



Foundation Wall SB2



Foundation insulation HB



Interior Cell Footers-HB



Concrete mixing tower on site



Completion of all Building Pads
This Photo by Hans Finke
