


**JAIL PROJECT  
JUNE STATUS REPORT TO BOARD OF SUPERVISORS**


**I. Achievements the past month**

**A. Construction:**

1. Site Work (Contractor: Ferguson Hall)
  - a. Building Pad for buildings units SB2 and Housing Unit HB shall be completed about June 24, approximately 5 days late.
  - b. Subsoil cut and fill work is 85% complete.
  - c. Contractor storage area should be near completion by the end of the month.
  - d. Installed approximately 900 feet of subsurface drainage below the future parking lot to drain springs (change order 1.01-2 processed by Board of Supervisors in May).
2. General Contractor (Horning Construction)
  - a. Began digging trenches and pouring concrete for building footings on Unit HB and SB2 during the last week of June. Rebar & forms received on site.
  - b. Submitted & received approval on all concrete mix designs, masonry accessories, rebar layout/reinforcement drawings.
3. Plumbing & Fire Suppression Contractor (Ferraulo Plumbing & Heating):
  - a. Mobilized trailer, material, & equipment the last week of June
  - b. Began work on underground piping.
  - c. Began fabrication of piping for cell chases off site.
4. Windows & Aluminum Storefront (The Glass Company): Submitted and received approval on security and non security glazing shop drawings.
5. HVAC Contractor (John W. Danforth):
  - a. Mobilized storage trailer and materials to job site.
  - b. Has begun fabrication of ductwork off site.
6. Electrical Contractor (Blackmon Farrell)
  - a. Completed pulling electric cables through duct bank from County Road 46 to transformer pad.
  - b. Transformer set on concrete pad at jail.
  - c. Switch gear behind the Youth Care Facility has been installed.
7. Precast Modular Cell Contractor (Oldcastle Precast): Submitted and received approval on precast cell geometry layout, erection, and structural load calculations.

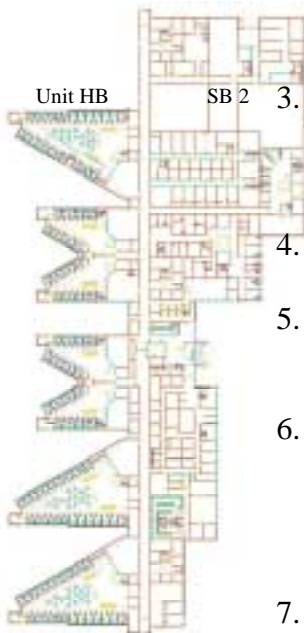

Progress



**B. Construction Manager (Pike Construction):** Held a preinstallation conference on June 19 to coordinate footing and foundation wall construction activities, including material testing contractor.

**C. Architect:**


1. Made color selections as follows:
  - a. Window frames at cell units: Chilean Red
  - b. Aluminum storefronts (window frames) adjacent to brick: Pueblo Tan
  - c. Exterior louvers (exhaust vents on exterior walls): bronze
  - d. Detention screens (in housing pods): bronze
  - e. Interior caulk and cell finish walls: tan
2. Processed 100 of 108 contractor requests for information to date. None are overdue.
3. Mechanical equipment (fan coil units, chillers, various pumps, and air handler units) have been reviewed and approved.

**D. Law Suit:**

1. Supreme Court: Motion to add the Canandaigua Messenger article to the record as evidence was denied from the bench.

Respectfully Submitted by Thomas P. Harvey AICP

**JAIL PROJECT  
JUNE STATUS REPORT TO BOARD OF SUPERVISORS**

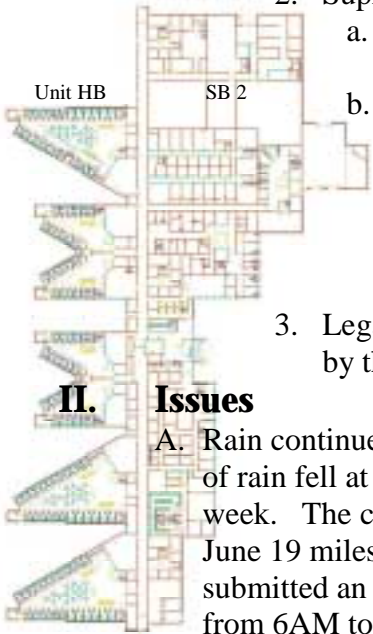

2. Supreme Court, Appellate Division, Fourth Judicial District
  - a. Motion to add the Canandaigua Messenger article to the record as evidence was denied.
  - b. Decision of Supreme Court affirmed in favor of the County. Written decision stated that the appellant (Noslen Corp. & John & Julie Sullivan), did not have standing. Court went on to state that even if the appellant had standing, the County complied with SEQR in that alternatives were considered and the appellant failed to allege any specific SEQR procedural error made by the County.
3. Legal Record: Will be publishing an article concerning the SEQR process employed by the County for the Jail as a model of how to do the process correctly.

**II. Issues**

- A. Rain continued to plague the project during the month of June; another approximately 5 inches of rain fell at the job site (through June 20). This has delayed the site work contractor about a week. The construction manager has issued notice to Ferguson Hall that they did not meet the June 19 milestone date for completion of the pad for building SB2 and HB. Ferguson Hall has submitted an official response that rain caused the delay. The Contractor has been working from 6AM to 6 PM and on Saturdays in an attempt to keep on schedule. Pike has made adjustments to the project schedule to accommodate this delay, which will not change the expected completion date.
- B. No-cost change orders will be processed in July or August to document the schedule changes.

**III. Planned for July**

- A. Construction Manager:
  1. Progress meetings held weekly on Tuesday mornings.
- B. Construction/Contractors
  1. Site work: Ferguson Hall is scheduled to complete remaining portions of the base for the buildings (building pads) during the first week of July. Water pipe installation may also begin.
  2. Electrical work: The contractor will begin underground electrical work under Housing Unit HB and Building SB2. This was delayed by rain during June.
  - 3.
  4. Plumbing Work: Michael Ferrauilo will continue underground piping work under Housing Unit HB and Building SB2.
  5. General Construction: Building HB & SB2 foundation walls to be built.
- C. Jail Project Committee: Bidding of mobile food carts (item that was taken out of Kitchen Contractors Bid).

**IV. Photos**



Switch Gear behind Youth Care Facility



HB building pad



Transformer



Soil stockpile
