


**JAIL PROJECT**  
**OCTOBER 1, 2002 STATUS REPORT TO BOARD OF SUPERVISORS**

**I. Achievements the past month (September)**

A. Construction:

1. Site Work (Contractor: Ferguson Hall): 8-inch waterlines, storm water, and sanitary sewer lines installed around building.
2. Precast masonry Cells (Oldcastle):
  - a. First Cells (Housing Unit HB) delivered and placed on September 23.
  - b. Interior finish paint thickened, double occupancy cell hardware strengthened in response to prototype cell review.
  - c. First & Second Floor Cells set in units HB, HC, & HD.
3. General Contractor (Horning Construction):
  - a. Completed masonry as follows: exterior and interior load bearing walls in SB-2, HC, HD, HE, & HF stair towers, and walls at showers and janitor closets in HB and first floor in HC & HD. Begun work on stair tower in HG.
  - b. Precast plank floor for mechanical room set.
4. Structural Steel & Miscellaneous Metal Contractor (Rochester Rigging & Erectors):  
SB 1 Began hanging roof joists in SB2 on September 26.
5. Plumbing & Fire Suppression Contractor (Ferrauilo Plumbing & Heating):
  - a. Underground piping (sanitary and water supply) completed in Housing unit HH.
  - b. All piping passed inspection and testing in HB, HE, HF, HG, & HH.
  - c. Began fire suppression piping installation in cell chases in HB.
6. HVAC Contractor (John W. Danforth): All ductwork in cell chases and in plenum in HB completed.
7. Electrical Contractor (Blackmon Farrell): Conduit stub-ups completed in HH.
8. Detention Equipment and Electronic Security (Maximum Security Products): Has delivered majority of door and window frames for all housing units and SB1 & SB6.

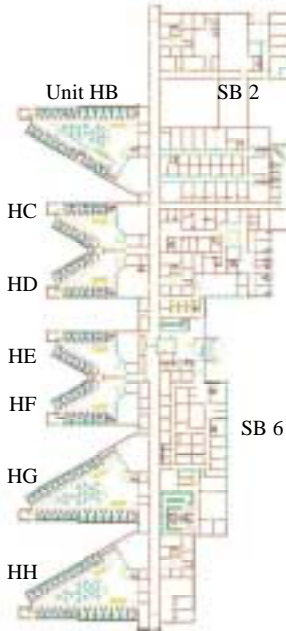

B. Construction Manager (Pike Construction):

1. Provided a new change order request to the County for additional waterline changes required by the Town of Hopewell (\$29,179.00).
2. Established a separate event log for tracking doorframe delivery by the Detention Equipment and Electronic Security Contractor, and a daily tracking of overtime work performed by the General Contractor and Electrical Contractor caused by doorframe delivery delays.

C. Architect:

1. Working on board of color selection for interior finishes.
2. Processed 209 of 210 contractor requests for information to date. None are overdue.
3. Completed revisions to exterior water piping plans in response to changes requested by the Town of Hopewell.


**II. Issues**

- A. Water service agreement with Hopewell/Canandaigua Water Districts.
- B. Delivery of Hollow Metal Doors by Maximum Security Products has lagged behind schedule. Additional work will be required by the General Contractor and Electrical Contractor as a result, but at no cost to the County. Catch-up work should be completed by October 12.

**III. Planned for October**

A. Construction/Contractors

1. Site work: Will install the remainder of the 16-inch waterline around the west side of the jail.



2. Precast: Cells for HE & HF scheduled for Oct. 10, HG on Oct. 21, and HH on Oct. 29. Precast plenum over cells in HB to begin Oct 9.
3. General Construction: SB1 exterior and interior load bearing walls to be completed on Oct 15, with walls in SB6 to follow after. HB, HE, & HF dayroom floor slab to be poured the week of Oct. 7, HC, HD, HH, & HG the week of Oct. 14.
4. Structural Steel: Joists and decking in SB2 to be completed, with SB1 to begin Oct. 16, and HB on Oct. 15.
5. Plumbing Work: Testing of piping in HC/HD scheduled for week of Oct. 16. Underground piping in SB6 to be completed. Fire suppression work in housing units will follow setting of cells in each housing unit.
6. HVAC: Cell chase ductwork in all housing units will begin on delivery and erection of cells. Heavy equipment such as the boiler and cooling tower to be set in SB2, air handlers in HB and possibly other housing units as cells and floor plank are set.
7. Electrical work: Conduit in cell chases will be done starting in HB and continuing in other housing units as cells are set, following ductwork completion by HVAC contractor. Back-up generator to be set and main power supply room work begun.
8. Detention Equipment: Will complete delivery of doorframes. Work with masons to install conduit for security equipment (door controls, monitors, intercom system) in concrete block walls in remaining Housing Units are erected.

B. Architect: Complete interior layout for water service room.

#### IV. Photos



First Cell Arrives on Truck



Setting first cell in HB



Two story cells installed in HB



Masonry wall sample



First steel roof joists set in SB2



First mezzanine plank in HB
